

NEW ORLEANS DISTRICT DREDGING SCHEDULE

FY 2017



®

US Army Corps of Engineers
BUILDING STRONG®



FY 2017 MVN Contract Dredging Schedule

FY 2017 New Orleans District Contract Dredging Schedule

- Cutterheads
- Hoppers
- Dustpans


FY 2017

Project	Manager	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP
Mississippi River Southwest Pass HDR #1-17	Kornick												
Mississippi River Southwest Pass Cutterhead #1-17	Kornick												
Mississippi River Southwest Pass HDR #2-17	Kornick												
Mississippi River Southwest Pass HDR #3-17	Kornick												
Mississippi River New Orleans Harbor CDR #1-17	Kornick/Landry												
Mississippi River New Orleans Harbor & Various Bars CDR #3-17 (Houma, Bayou Lafourche, & Baptiste Collette)	Newman												
Atchafalaya Basin, GIWW, and Miscellaneous Projects IDIQ	Connell/Landry/Beauvais												
Atchafalaya River CDR #1-17	Connell												
Calcasieu River Mi. 17-34	Falk												





MISSISSIPPI RIVER Southwest Pass

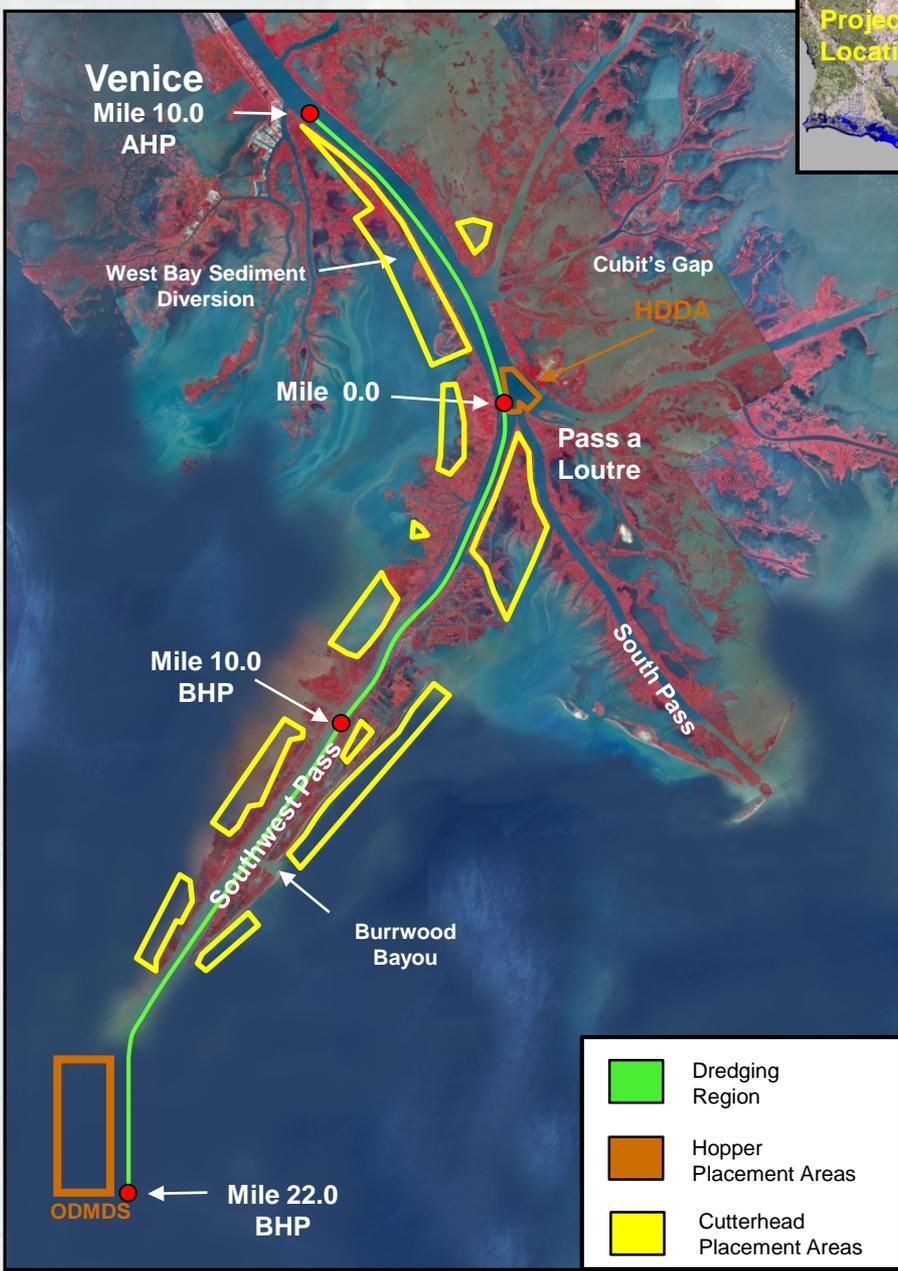

Type of Equipment:

Hopper / Cutterhead

Schedule: Based on River Stage

Depth: 45 ft

Width: 600 ft – 750 ft

Quantity: 17.5M cy (Annual Avg)

Placement Area:

Open Water, Wetland Development

- HDDA at Head of Passes
- ODMDS
- Shallow open water areas located on either side of the channel


Last Dredged: 2016



MISSISSIPPI RIVER

New Orleans Harbor

Algiers, Harvey & IHNC Lock Forebays

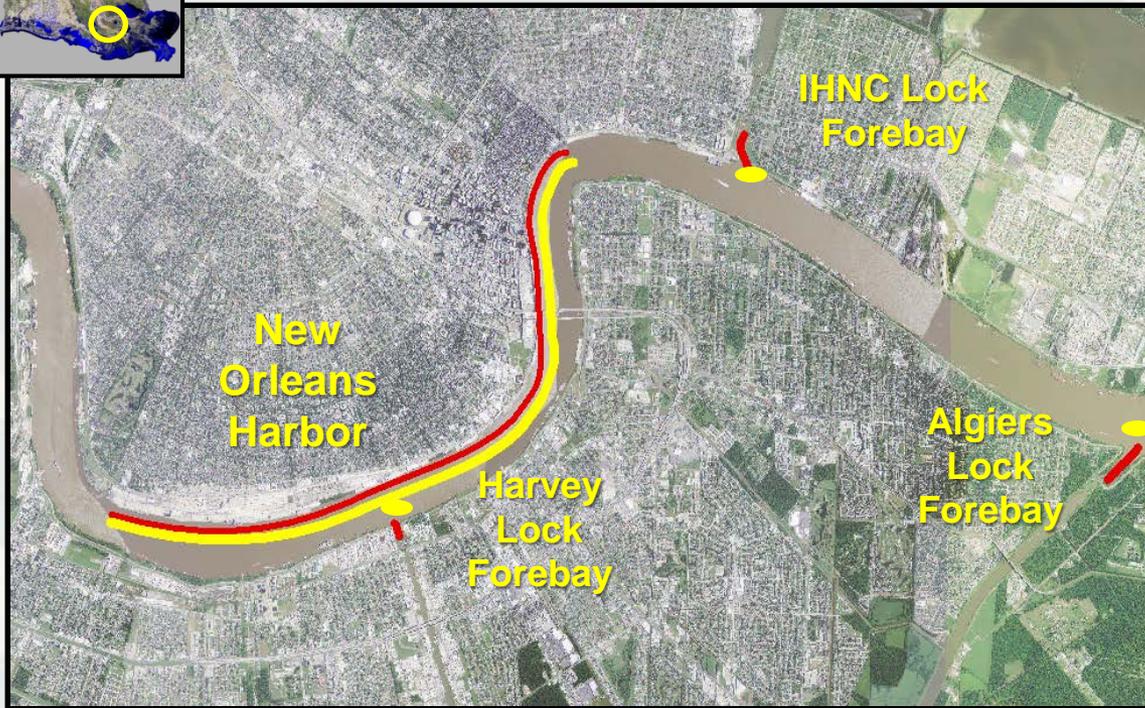

-  Open Water Placement
-  Dredging Region

Type of Equipment: Cutterhead

Schedule: Based on River Stage

Depth: Varies by location
15 ft to 35 ft

Quantity: (Annual Avg)
Harbor - 500K cy
Locks - 100K cy

Placement Area: Open Water

Last Dredged: 2016



Operations Managers: Mississippi River, Michelle Kornick 504-862-1842
GIWW, Vic Landry 504-862-2407

BUILDING STRONG®

HOUMA NAVIGATION CANAL Terrebonne Bay

Mississippi River New Orleans Harbor
and Various Bars #3-2016

Type of Equipment: Cutterhead

Schedule: Jul 2017


Depth: 18 ft

Width: 150 ft

Quantity: 150K cy

Placement Area: Open Water

Last Dredged: 2016

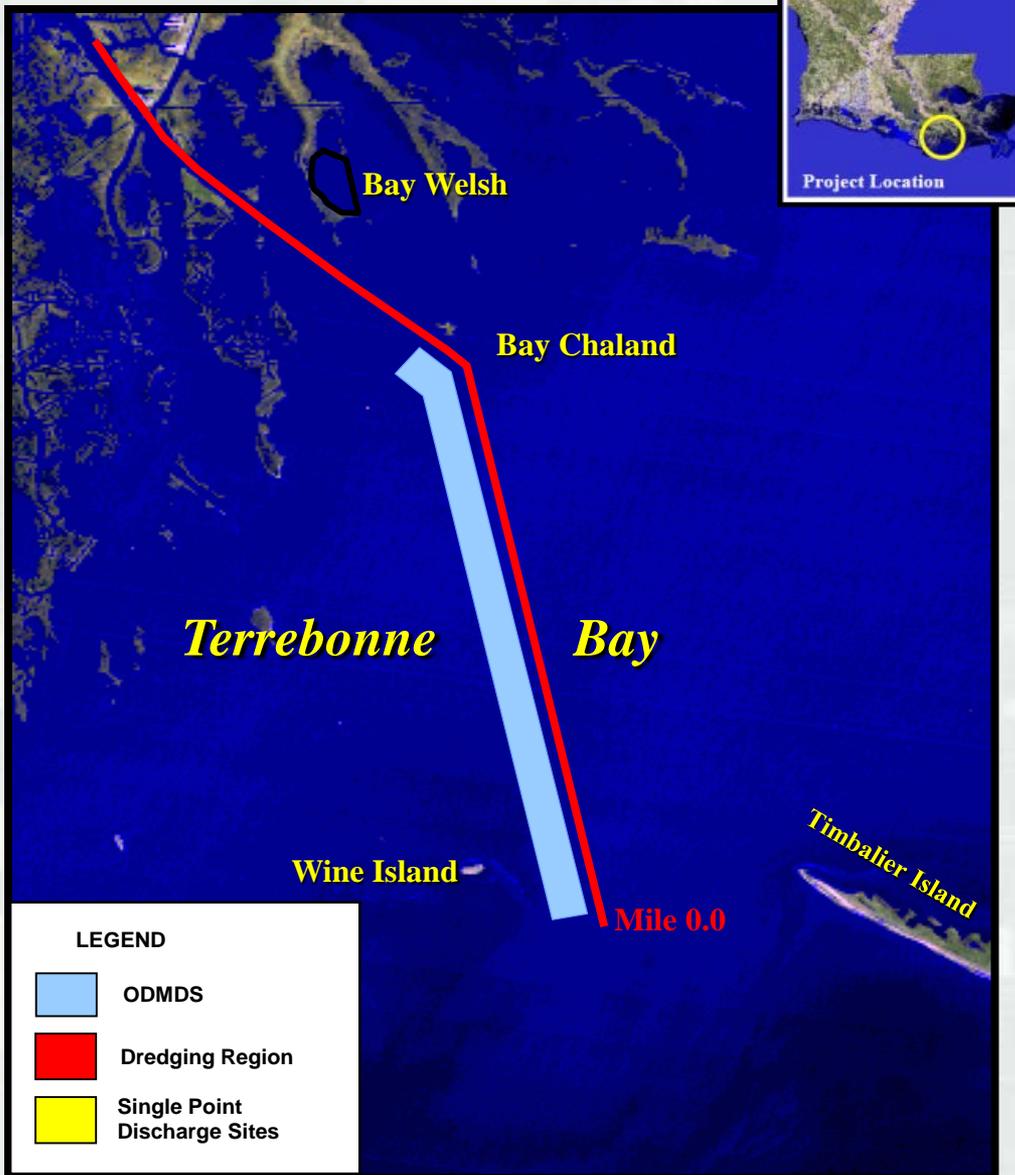

Operations Manager: Ray Newman 504-862-2050

BUILDING STRONG®



BAYOU LAFOURCHE

Bar Channel

Mississippi River New Orleans Harbor
and Various Bars #3-2016

Type of Equipment: Cutterhead

Schedule: Jul 2017

Depth: 27 ft – 30 ft

Width: 300 ft


Quantity: 150K cy

Placement Area: Shoreline

Nourishment

Last Dredged: 2014



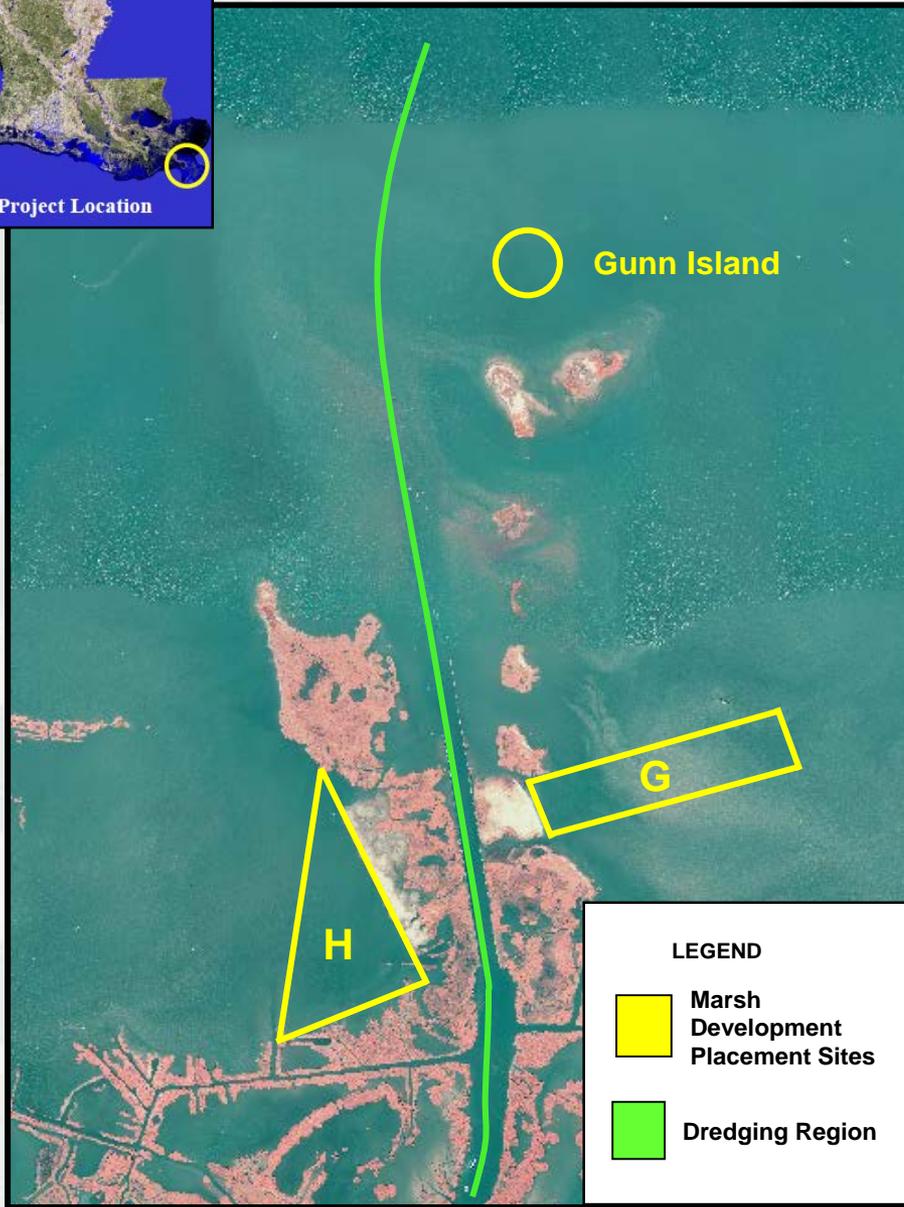

BAPTISTE COLLETTE

Bar Channel

Mississippi River New Orleans Harbor
and Various Bars #3-2016

Type of Equipment: Cutterhead

Schedule: Aug 2017

Depth: 16 ft – 18 ft

Width: 150 ft – 250 ft

Quantity: 300k cy


Placement Area:

Wetlands Development, Bird Island

Last Dredged: 2016



ATCHAFALAYA BASIN GIWW & MISC PROJECTS

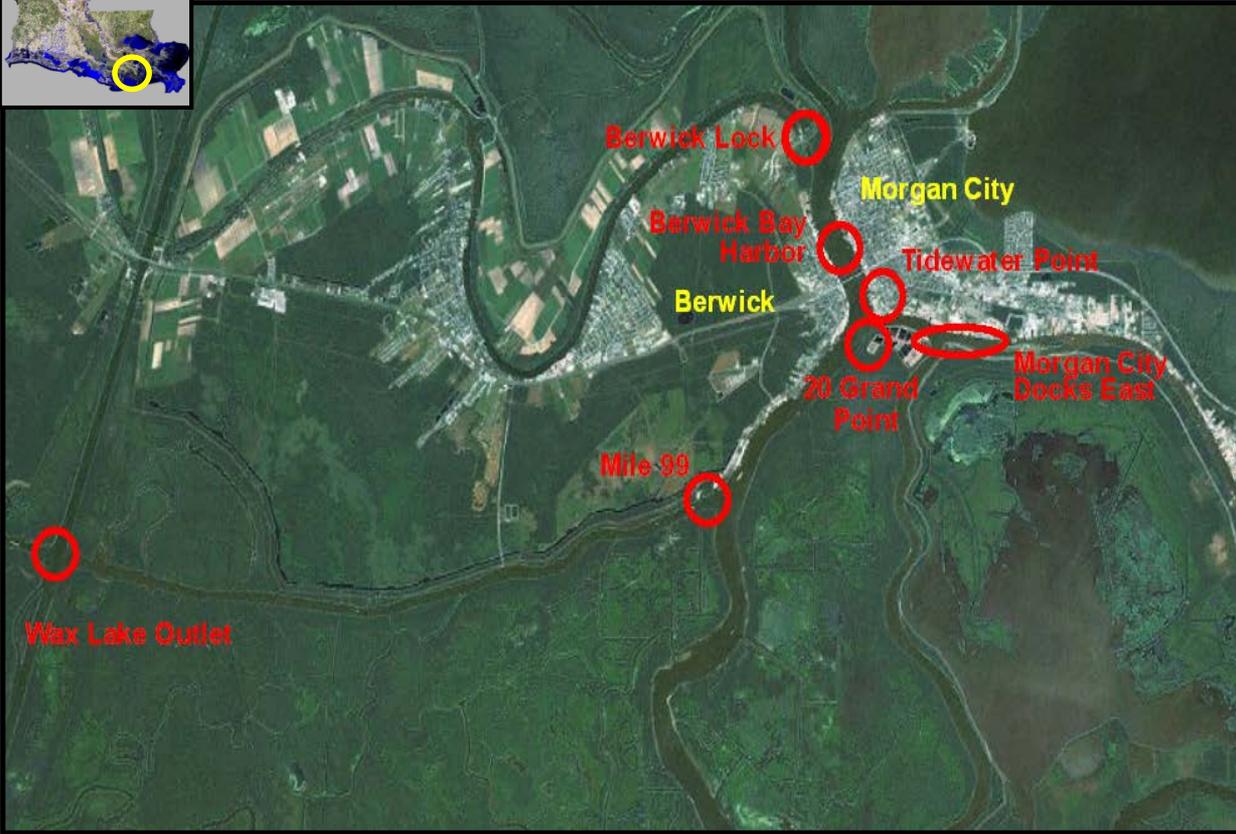

Type of Equipment: Cutterhead
Schedule: Jun - Oct 2017
Depth: 12 ft to 16 ft
Width: Various
Quantity: 1.2M cy
Placement Areas:
Open Water
Sand Pits (Berwick Harbor)
Last Dredged: 2016

 Dredging Region

Dredging Locations: Berwick Bay Harbor, Berwick Lock, Tidewater Point, 20 Grand Point, Morgan City Docks East, Mile 99, Wax Lake Outlet
(continued on next slide)




Operations Managers: Atchafalaya, Tim Connell 504-862-2360
GIWW, Vic Landry 504-862-2407
Old River, Russell Beauvais 225-492-2169

BUILDING STRONG®

ATCHAFALAYA BASIN GIWW & MISC PROJECTS (continued)

Dredging Locations: Port Allen Lock Forebay, Baton Rouge Harbor (Devil's Swamp), Old River Lock Forebay & Tailbay and Three Rivers

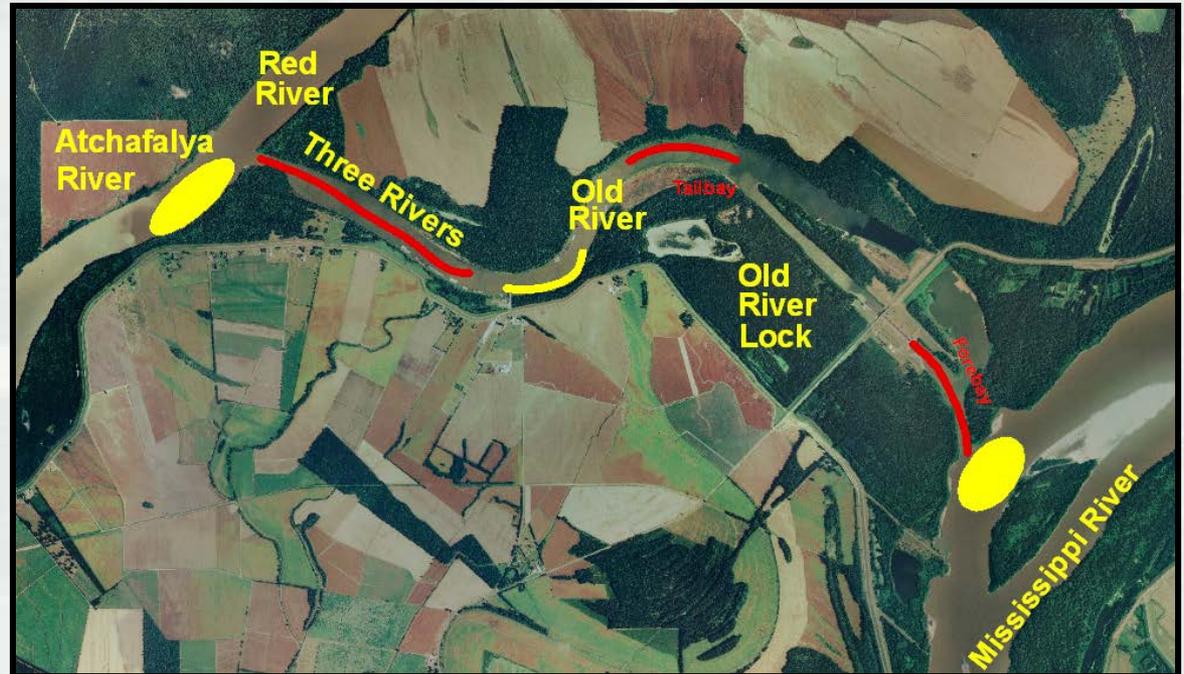


- Open Water Placement
- Dredging Region



Operations Managers: Atchafalaya, Tim Connell 504-862-2360
GIWW, Vic Landry 504-862-2407
Old River, Russell Beauvais 225-492-2169

BUILDING STRONG®

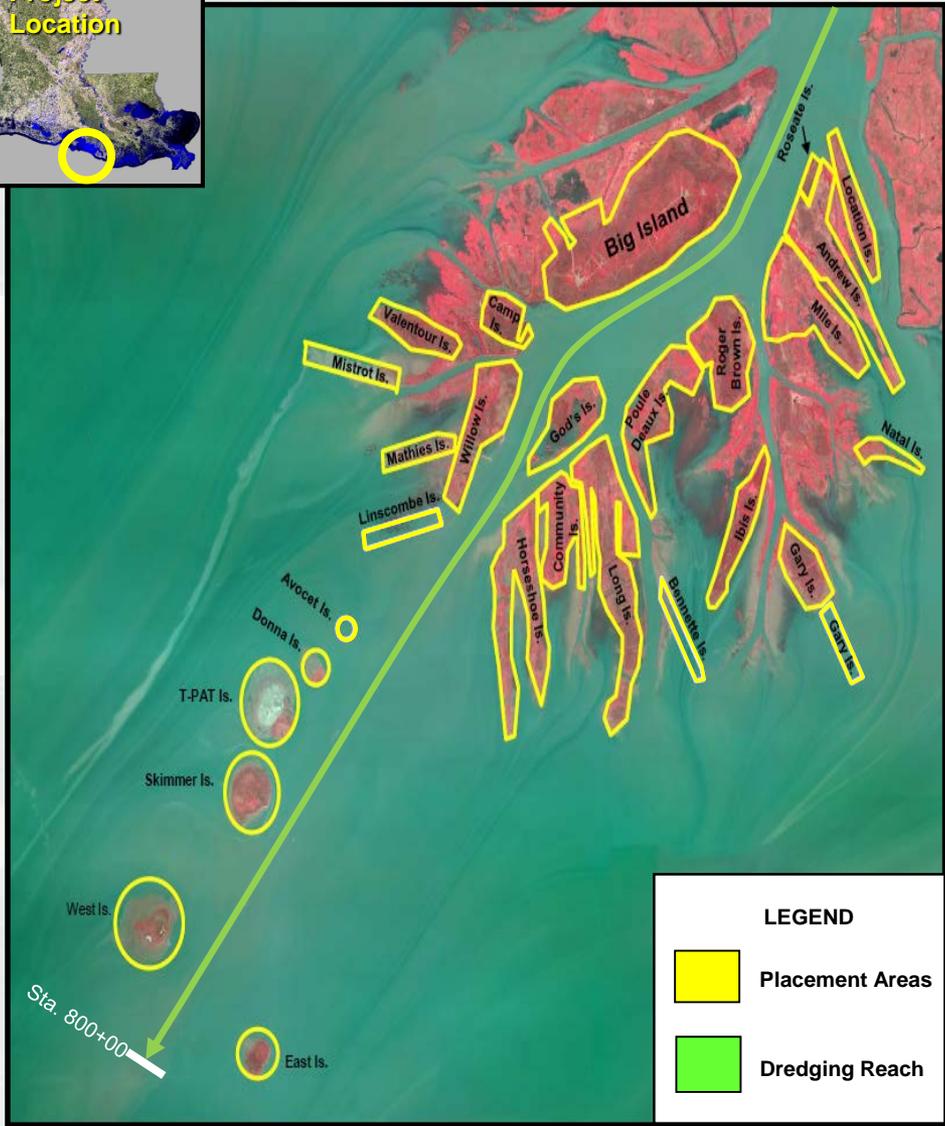

ATCHAFALAYA RIVER Bay & Bar

Type of Equipment: Cutterhead

Scheduled: Aug - Nov 2017

Quantity: 3M cy

Bay: 20 ft x 400 ft


Placement Area: Open Water Island Creation

Bar: 20 ft x 400 ft

Placement Area: Bird Island

Last Dredged: 2015



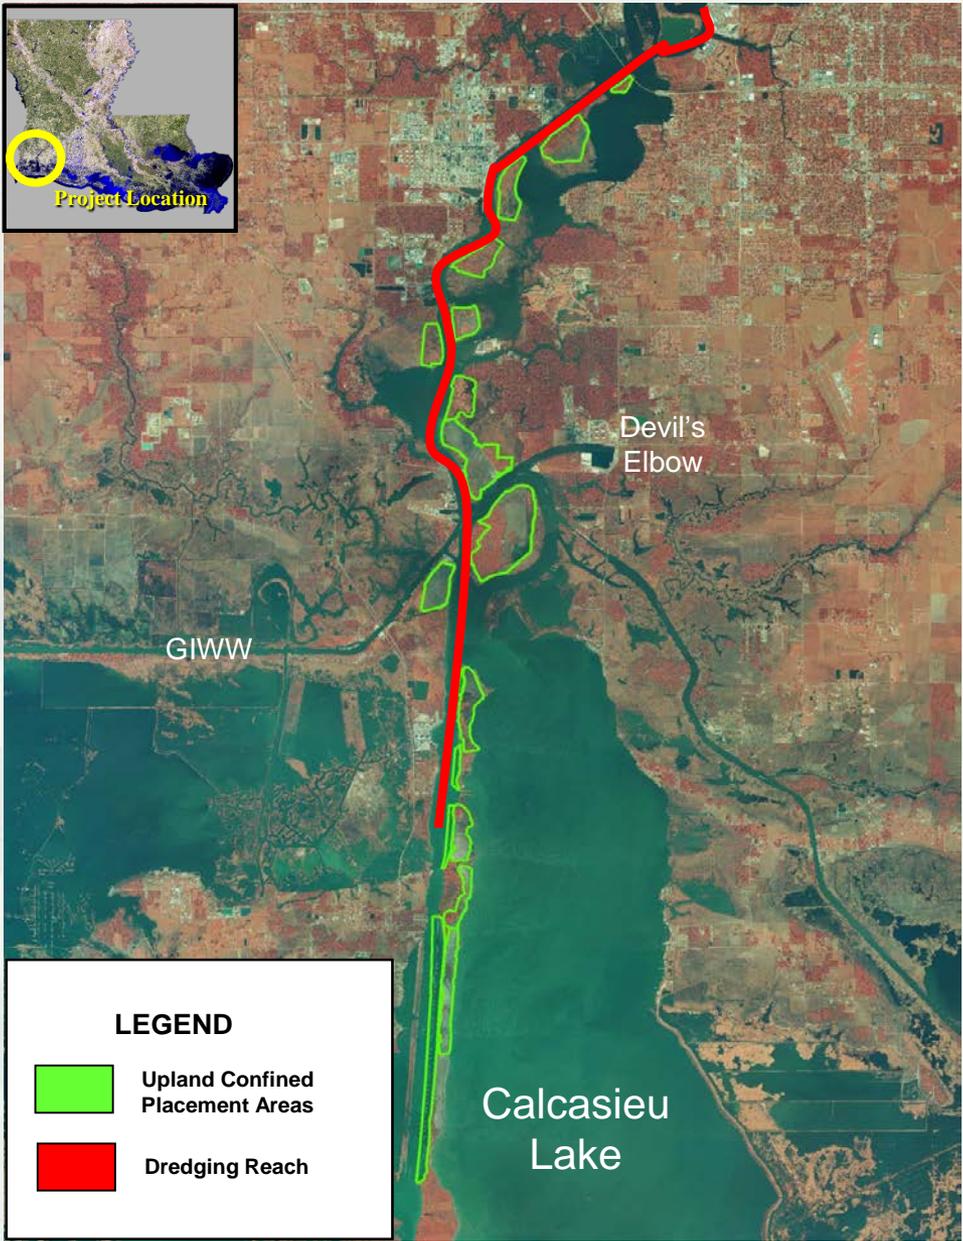

CALCASIEU RIVER

Vicinity Miles 17 – 34

Type of Equipment: Cutterhead

Schedule: Aug 2017 – Jun 2018

Depth: 40 ft

Width: 400 ft

Quantity: 4.5M cy

Placement Area: Upland CDF's

Last Dredged: 2016

